

**RAPID RESPONSE WEEKLY REPORT**

**Project Name -** Poleline Road Disposal Area                      **Week ending -** 9-10-94

**Project Location -** Fort Richardson, Alaska                      **Report No. -** 008

**Prepared by -** OHM Remediation Services Inc.                      **Reporting Period** 9-7-94 thru 9-10-94

**Percent Field Work Completed -** 75 %                      **Percent Project Completed -** 70 %

**Summary of Work Completed On Site -**

1. This was a short work week due to personnel returning from the scheduled Labor Day Turnaround.
2. All excavation this week was in Area A-4, Zone 10.
3. On Wednesday the 7th, items removed from the excavation included:
 

1 - HC Smoke Pot	2 - 105mm artillery rounds
8 - M51 Smoke Pots	1 - Nose fuse
2- M-18 Smoke Grenades	Several - CN ID Set Bottles
1- Rifle Grenade Fuse	
4. On Thursday very little ordnance was found. There were large amounts of scrap metal from rusted buckets, cans, etc.
5. On Friday we continued to find scrap metal and 3- empty 105mm casings.
6. On Saturday the 10th, the following items were excavated:
 

2 - small lecture bottles	1- 1/2 gallon amber jar with no lid, empty
5 - empty 55 gallon drums	5 - Flame thrower cannisters
Assorted metal debris	
7. We have moved all organic contaminated soil temporary soil piles which have been identified to be over the action level, to one permanent lined storage cell. Approximately 1600 yards have been moved to date.

**Summary of Work Completed Off Site -**

None

**Explanation of Deviation from Work Plan -**

NONE

**Problems Encountered -**

NONE

**Recommendations -**

NONE

**Key Personnel Changes -**

NONE

**Work Anticipated to be Performed Next Week -  
ther Remarks -**


1. Complete excavation in Area A-4.
2. Re-excavate north end of Zone 7 to remove organic solvent hot spot
3. Complete removal of small amount soil from north east side wall of Zone 7
4. Re-excavate south east end near monitoring well 5.
5. Begin re-excavation of organic contaminated soil from bottom of Area A-3
6. Demobilize Tech Escort, Fire Department, Medics, and OHM air monitoring team.

Submitted



Larry Hudson  
Project Manager  
OHM Remediation Services

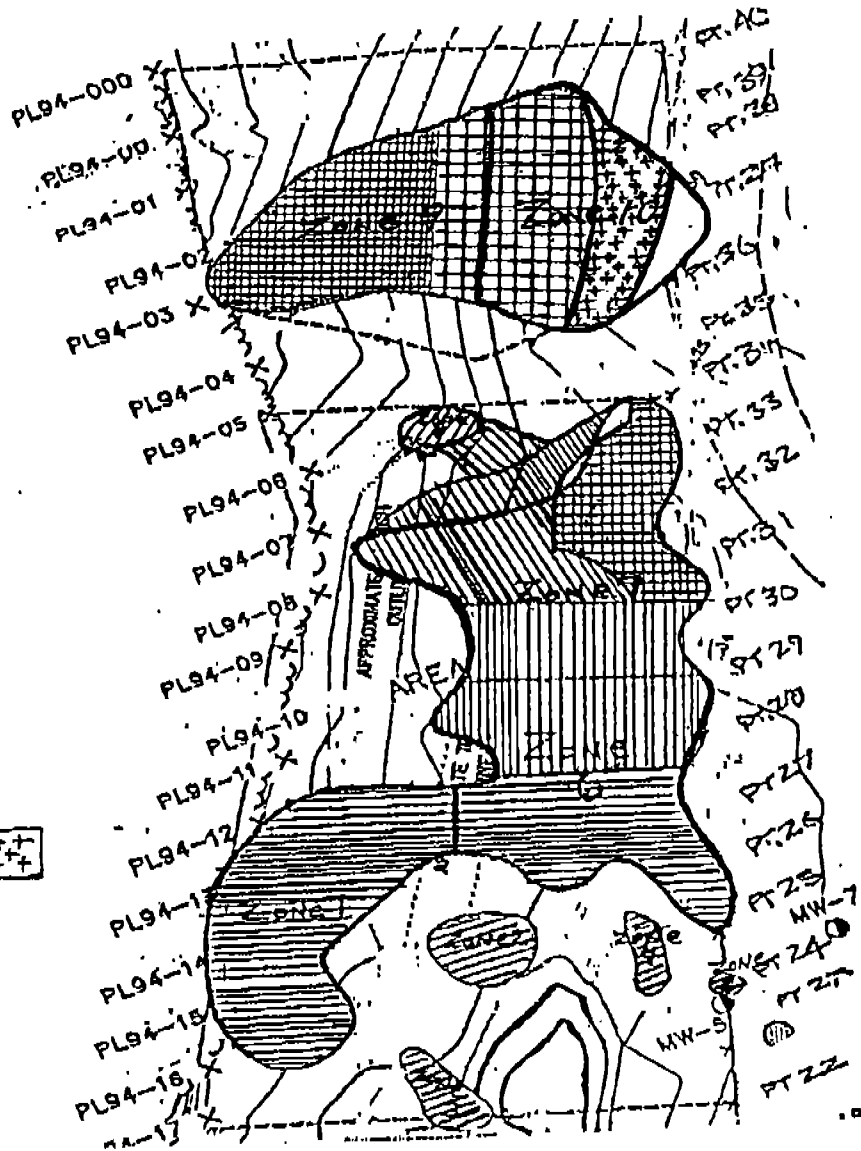
Approved








Steve Dawson  
Construction Representative  
U.S. Army Corps of Engineers

# Poleline Road Zone Delineation

9-12-94



Week 8-Progress 

- Week 3 Progress To Date 
- Week 4 Progress 
- Week 5 Progress 
- Week 6 Progress 
- Week 7 Progress 
